



Revitalisation Project Update 19 February 2026

Dear St Michael's Community,

This week's site visit has given us insight into the exciting work progression in the church auditorium, toilet amenities, entry and in St Michael's walk.

In the auditorium additional floor levelling has been completed in the upper tiered seating, to reduce undulation in the floor and improve the substrate for carpet install over. The carpet underlay has been installed to the majority of the auditorium, and we will see the new carpet install starting from next week. We can see that the electric heating coil installation have commenced to the lower floor, so we will keep warm in the winter mornings.

The curved nosing detail to half-moon stage has been templated for manufacturing and new timber detailing has been installed along the pulpit panelling, ready for carpet install.

The toilet amenities stud frame walls have now been insulated and will soon have fresh plasterboard sheeting installed. The hardwood door frames have been fitted to toilet doors.

The new opening to the choir vestry has been completed and the switch room has been enclosed. Inside the switch room we are pleased with modern, up-to-date meter and switchboards.

At the South Lobby and entries the floor is being levelled making for a smooth and easy entry into the church. Outside I St Michael's Walk the retaining wall is complete and backfilled. The next step will be to lay the concrete slab over.

What's happening in the auditorium?




Additional floor levelling has been completed in the upper tiered seating




Underlay has been installed to the majority of the auditorium



Electric heating coil installation on the lower floor

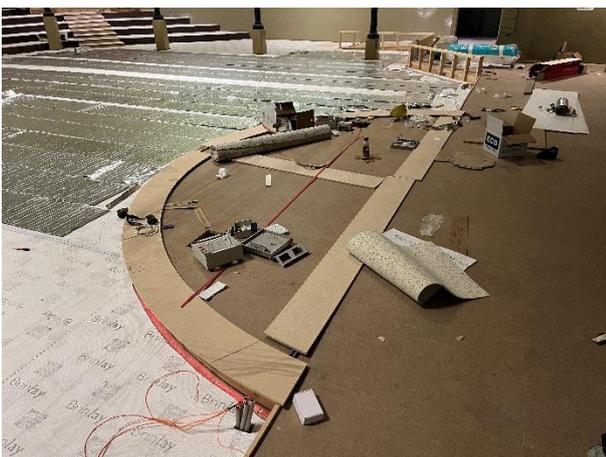

The curved nosing detail on stage templated for manufacturing

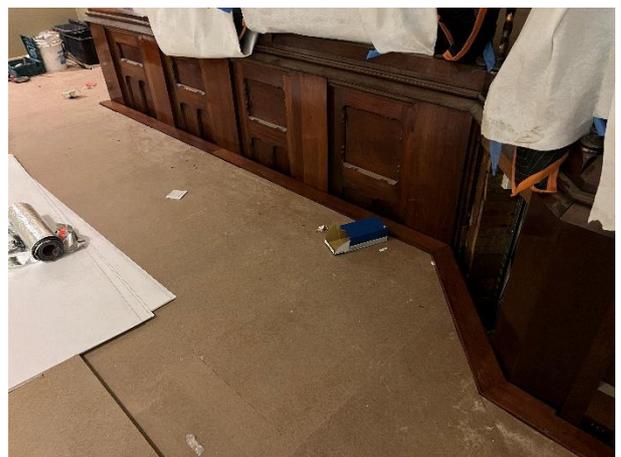

New timber detailing installed along pulpit panelling
